ID	Task Mode	Task Name	Duration	Start	Finish	% Comp.	Baseline Cost	Resource Names	Predecessors
0		**Webook**	**68.5 days**	**Fri 1/10/21**	**Tue 30/11/21**	**100%**	**$45,839.29**		
1		**1 Requirement Phase**	**10.38 days**	**Fri 1/10/21**	**Sun 10/10/21**	**100%**	**$21,982.14**		
2		1.1 Team Bonding	2 hrs	Fri 1/10/21	Fri 1/10/21	100%	$214.29	Christie;Danial;Hui Min;Tian	
3		1.2 Project Charter	4 hrs	Fri 1/10/21	Fri 1/10/21	100%	$428.57	Christie;Danial;Hui Min;Tian	2
4		1.3 CIO Approval	1 hr	Fri 1/10/21	Fri 1/10/21	100%	$17.86	Christie	2
5		1.4 Project Scope	3 hrs	Sat 2/10/21	Sat 2/10/21	100%	$321.43	Christie;Danial;Hui Min;Tian	4
6		1.5 Purchase Computers	1 day	Sun 3/10/21	Sun 3/10/21	100%	$9,000.00	Computers[6]	
7		1.6 Learn Basic Coding	1 wk	Mon 4/10/21	Sun 10/10/21	100%	$6,000.00	Christie[30%];Danial[Min[30%];Tian	
8		1.7 Learn Basic GUI	1 wk	Mon 4/10/21	Sun 10/10/21	100%	$6,000.00	Christie[30%];Danial[Min[30%];Tian	
9		1.8 Requirements	0 days	Sun 10/10/21	Sun 10/10/21	100%	$0.00		8
10		**2 Coding Phase**	**17.38 days**	**Wed 13/10/21**	**Thu 28/10/21**	**100%**	**$4,285.74**		
11		2.1 Coding of Student End	5 days	Wed 13/10/21	Sun 17/10/21	100%	$1,428.58	Danial[30%];Whye Keat[30%]	

Project: Webook
Date: Fri 12/11/21



ID	Task Mode	Task Name	Duration	Start	Finish	% Comp.	Baseline Cost	Resource Names	Predecessors
12		2.2 Coding of Staff End	5 days	Wed 13/10/21	Sun 17/10/21	100%	$1,428.58	Danial[30%];Whye Keat[30%]	
13		2.3 Coding of System Admin	5 days	Sun 24/10/21	Thu 28/10/21	100%	$1,428.58	Whye Keat[35%];Danial[35	
14		2.4 Coding Complete	0 days	Sun 17/10/21	Sun 17/10/21	100%	$0.00		12
15		**3 Integration Phase**	**5 days**	**Tue 19/10/21**	**Sat 23/10/21**	**100%**	**$1,428.57**		
16		3.1 Convert C++ into Python	3 days	Tue 19/10/21	Thu 21/10/21	100%	$857.14	Danial;Whye Keat	
17		3.2 Display code in GUI	2 days	Thu 21/10/21	Sat 23/10/21	100%	$571.43	Christie;Hui Min	16
18		3.3 Integration Complete	0 days	Sat 23/10/21	Sat 23/10/21	100%	$0.00		17
19		**4 Testing Phase**	**43.25 days**	**Sat 23/10/21**	**Tue 30/11/21**	**100%**	**$1,714.28**		
20		4.1 Testing Student End	1 day	Sat 23/10/21	Sun 24/10/21	100%	$285.71	Christie[35%];Hui Min[35%]	18
21		4.2 Testing Staff End	1 day	Sat 23/10/21	Sun 24/10/21	100%	$285.71	Tian Sheng;Yong Qi	18
22		4.3 Testing of System Admin End	1 day	Tue 30/11/21	Tue 30/11/21	100%	$285.71	Danial;Whye Keat	
23		4.4 Testing Integrated	2 days	Sun 24/10/21	Tue 26/10/21	100%	$571.43	Christie;Yong Qi	21

Project: Webook
Date: Fri 12/11/21



ID	Task Mode	Task Name	Duration	Start	Finish	% Comp.	Baseline Cost	Resource Names	Predecessors
24		4.5 Testing Codes on GUI	1 day	Tue 26/10/21	Tue 26/10/21	100%	$285.71	Hui Min;Tian Sheng	23
25		4.6 Testing Complete	0 days	Tue 26/10/21	Tue 26/10/21	100%	$0.00		24
26		**5 Documentation Phase**	**5.25 days**	**Wed 27/10/21**	**Sun 31/10/21**	**100%**	**$2,571.43**		
27		5.1 Prepare Report	2 days	Wed 27/10/21	Thu 28/10/21	100%	$571.43	Christie;Hui Min	25
28		5.2 Prepare Video	2 days	Wed 27/10/21	Thu 28/10/21	100%	$571.43	Danial[50%];Whye Keat[50%]	25
29		5.3 Prepare Delivarables	2 days	Fri 29/10/21	Sat 30/10/21	100%	$571.43	Tian Sheng;Yong Qi	28
30		5.4 Prepare for Q&A with CIO	2 days	Fri 29/10/21	Sat 30/10/21	100%	$571.43	Hui Min[50%];Danial[50%	28
31		5.5 Quality Control	1 day	Sat 30/10/21	Sun 31/10/21	100%	$285.71	Whye Keat[50%];Christie[5(	30
32		5.6 Documentation	0 days	Sun 31/10/21	Sun 31/10/21	100%	$0.00		31
33		**6 Project Closing**	**7.88 days**	**Wed 3/11/21**	**Tue 9/11/21**	**100%**	**$857.14**		
34		6.1 Submission of Report	2 days	Wed 3/11/21	Thu 4/11/21	100%	$285.71	Christie;Danial	32
35		6.2 Submission of Video	2 days	Fri 5/11/21	Sat 6/11/21	100%	$285.71	Hui Min;Yong Qi	34

Project: Webook
Date: Fri 12/11/21



ID	Task Mode	Task Name	Duration	Start	Finish	% Comp.	Baseline Cost	Resource Names	Predecessors
36		6.3 Submission of Deliverables	3 days	Sun 7/11/21	Tue 9/11/21	100%	$285.71	Tian Sheng;Whye Keat	35
37		6.4 Project Close	0 days	Tue 9/11/21	Tue 9/11/21	100%	$0.00		36
38		**7 Office Payment**	**47.25 days**	**Mon 4/10/21**	**Mon 15/11/21**	**100%**	**$7,000.00**		
39		7.1 Office Payment 1	0 days	Mon 4/10/21	Mon 4/10/21	100%	$1,000.00	Office Rental	
40		7.2 Office Payment 2	0 days	Mon 11/10/21	Mon 11/10/21	100%	$1,000.00	Office Rental	
41		7.3 Office Payment 3	0 days	Mon 18/10/21	Mon 18/10/21	100%	$1,000.00	Office Rental	
42		7.4 Office Payment 4	0 days	Mon 25/10/21	Mon 25/10/21	100%	$1,000.00	Office Rental	
43		7.5 Office Payment 5	0 days	Mon 1/11/21	Mon 1/11/21	100%	$1,000.00	Office Rental	
44		7.6 Office Payment 6	0 days	Mon 8/11/21	Mon 8/11/21	100%	$1,000.00	Office Rental	
45		7.7 Office Payment 7	0 days	Mon 15/11/21	Mon 15/11/21	100%	$1,000.00	Office Rental	
46		**8 Team Meeting**	**48.25 days**	**Sat 2/10/21**	**Sat 13/11/21**	**100%**	**$5,999.98**		
47		8.1 Team Meeting 1	1 day	Sat 2/10/21	Sat 2/10/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	

Project: Webook
Date: Fri 12/11/21



ID	Task Mode	Task Name	Duration	Start	Finish	% Comp.	Baseline Cost	Resource Names	Predecessors
48		8.2 Team Meeting 2	1 day	Mon 11/10/21	Mon 11/10/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	
49		8.3 Team Meeting 3	1 day	Sat 16/10/21	Sat 16/10/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	
50		8.4 Team Meeting 4	1 day	Sat 23/10/21	Sat 23/10/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	
51		8.5 Team Meeting 5	1 day	Sat 30/10/21	Sat 30/10/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	
52		8.6 Team Meeting 6	1 day	Sat 6/11/21	Sat 6/11/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	
53		8.7 Team Meeting 7	1 day	Sat 13/11/21	Sat 13/11/21	100%	$857.14	Christie[5%];Danial[5 Min[5%];Tian	

25

Project: Webook
Date: Fri 12/11/21



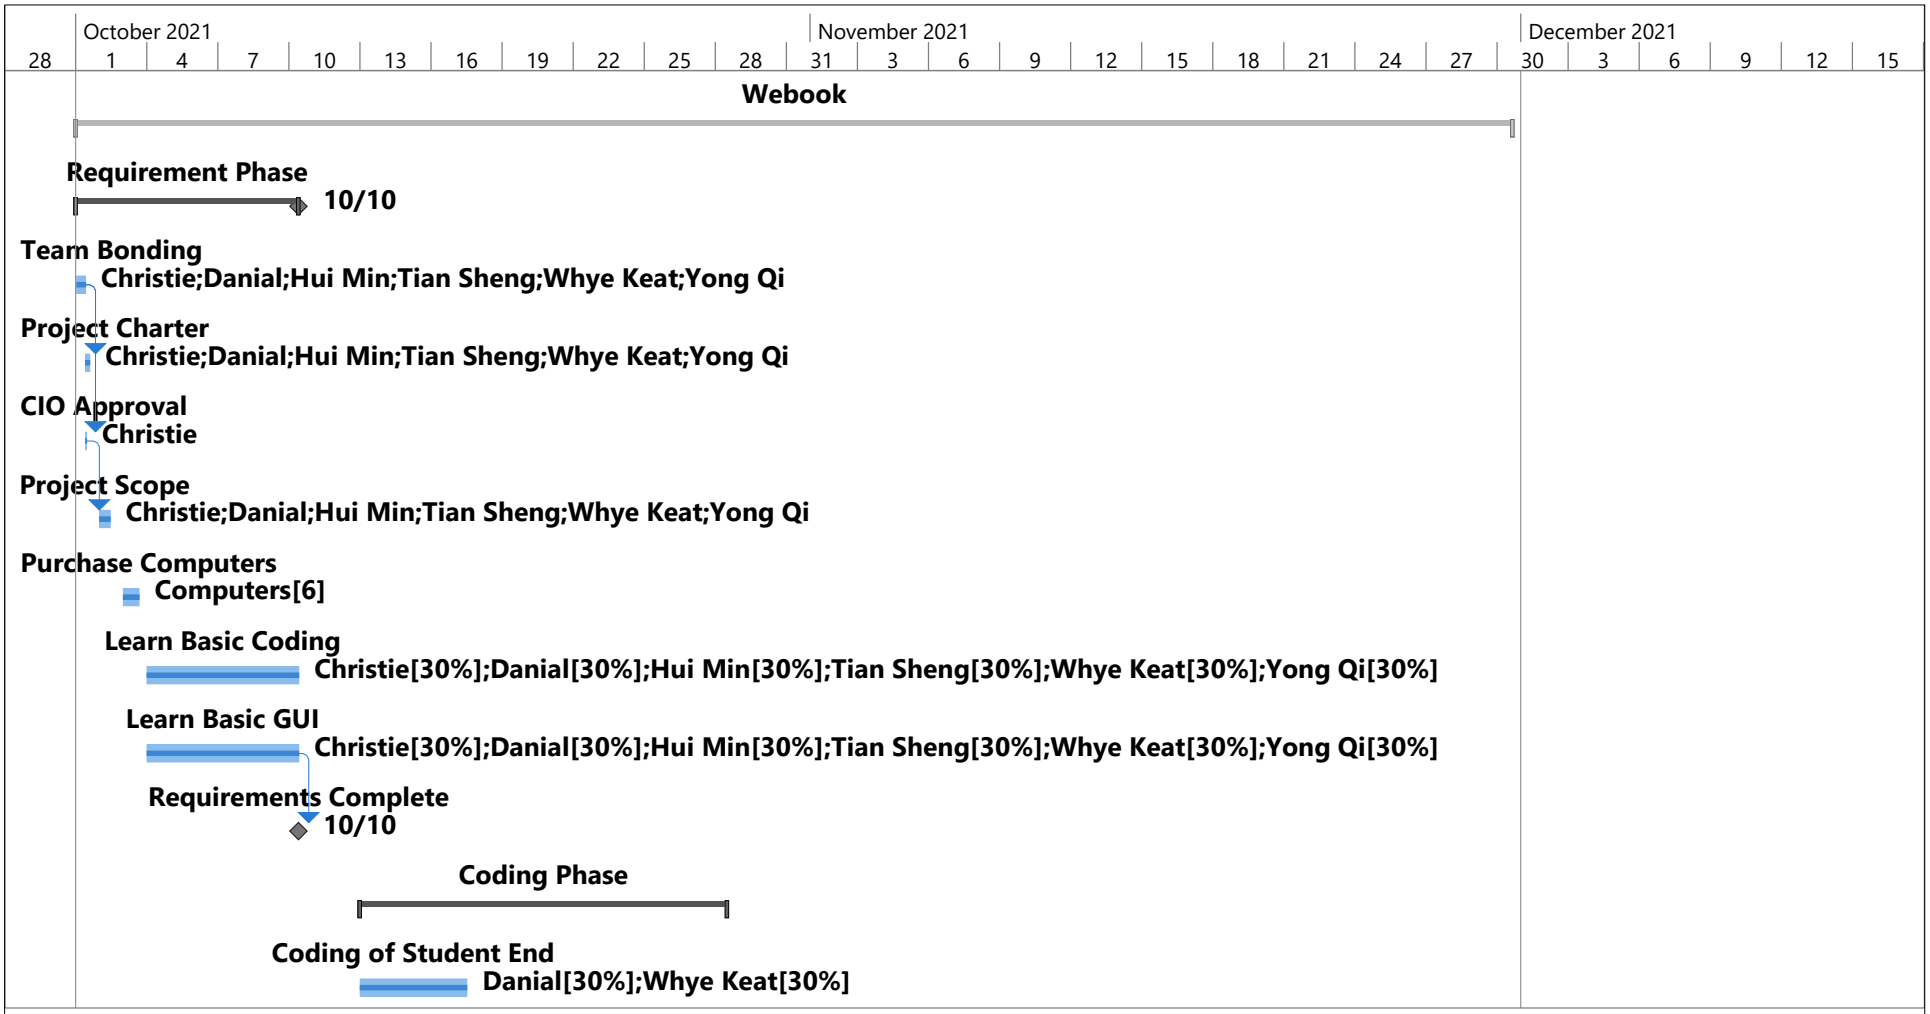

Project: Webook
Date: Fri 12/11/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

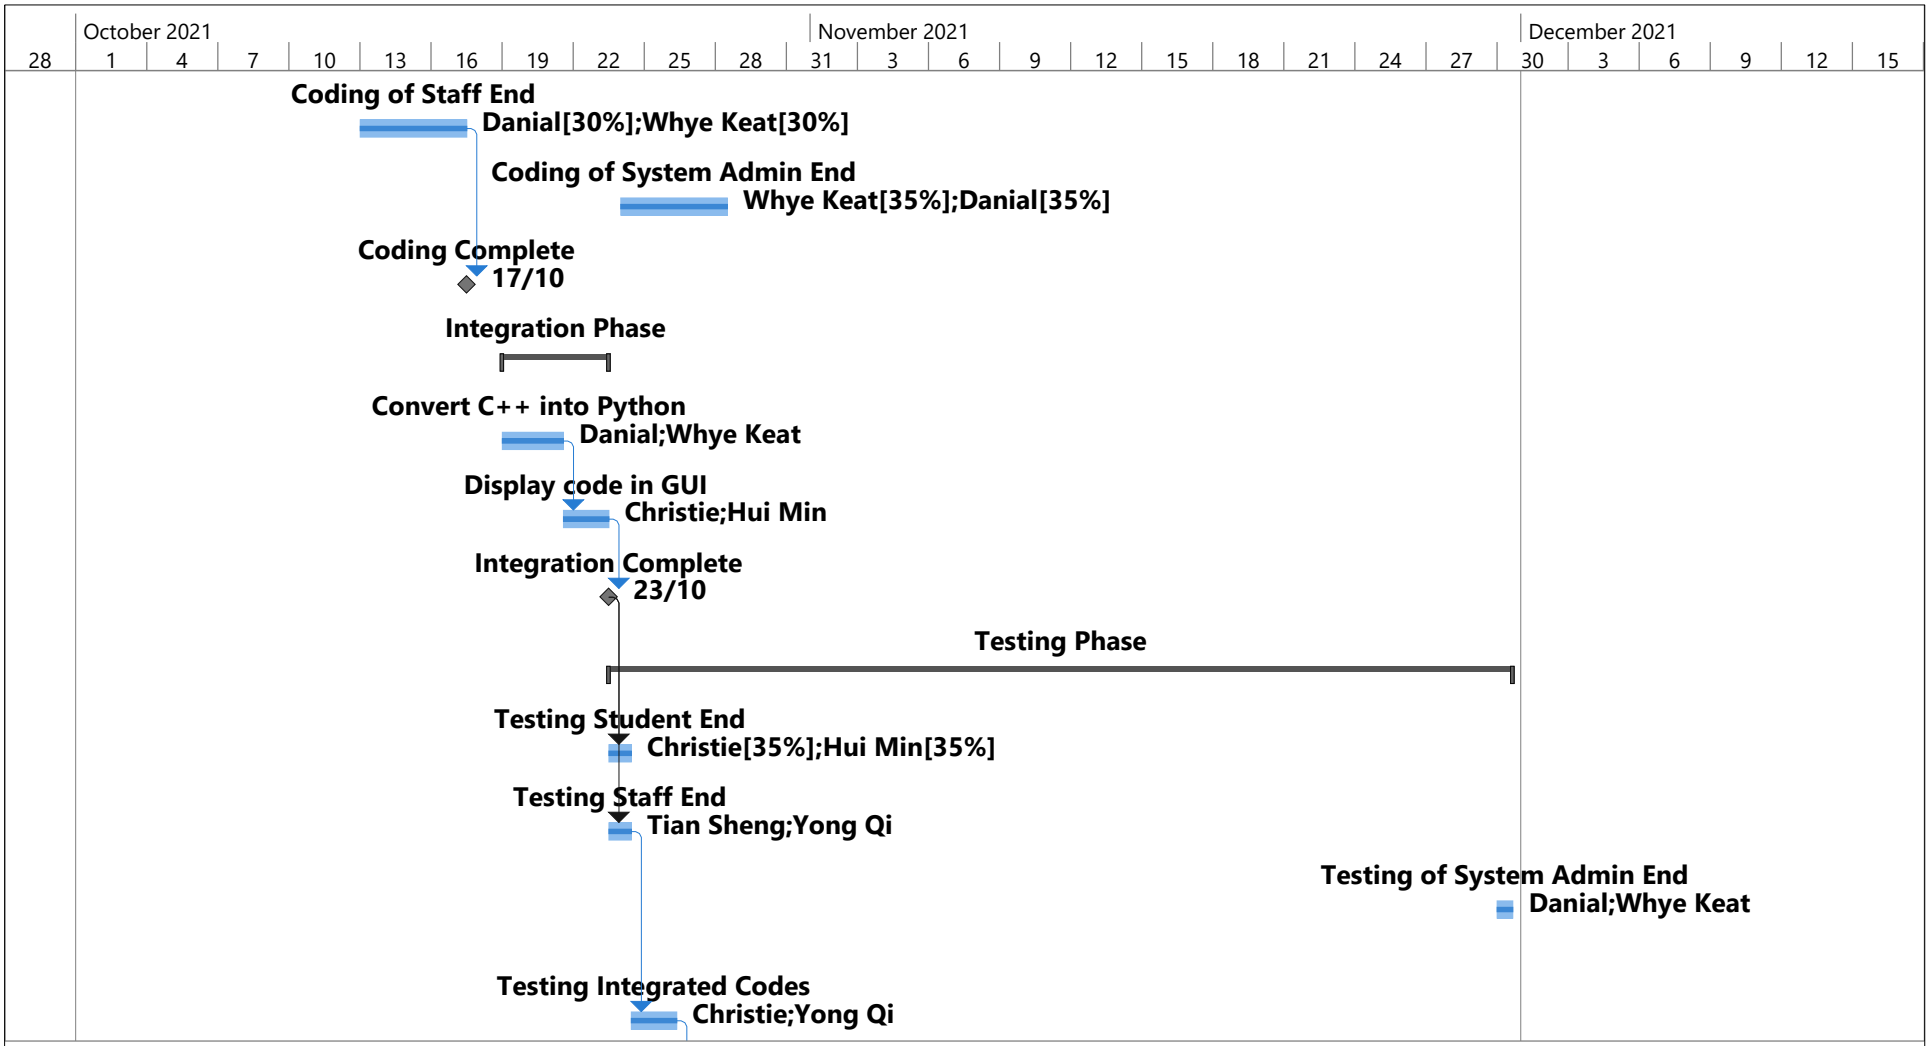

Project: Webook
Date: Fri 12/11/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

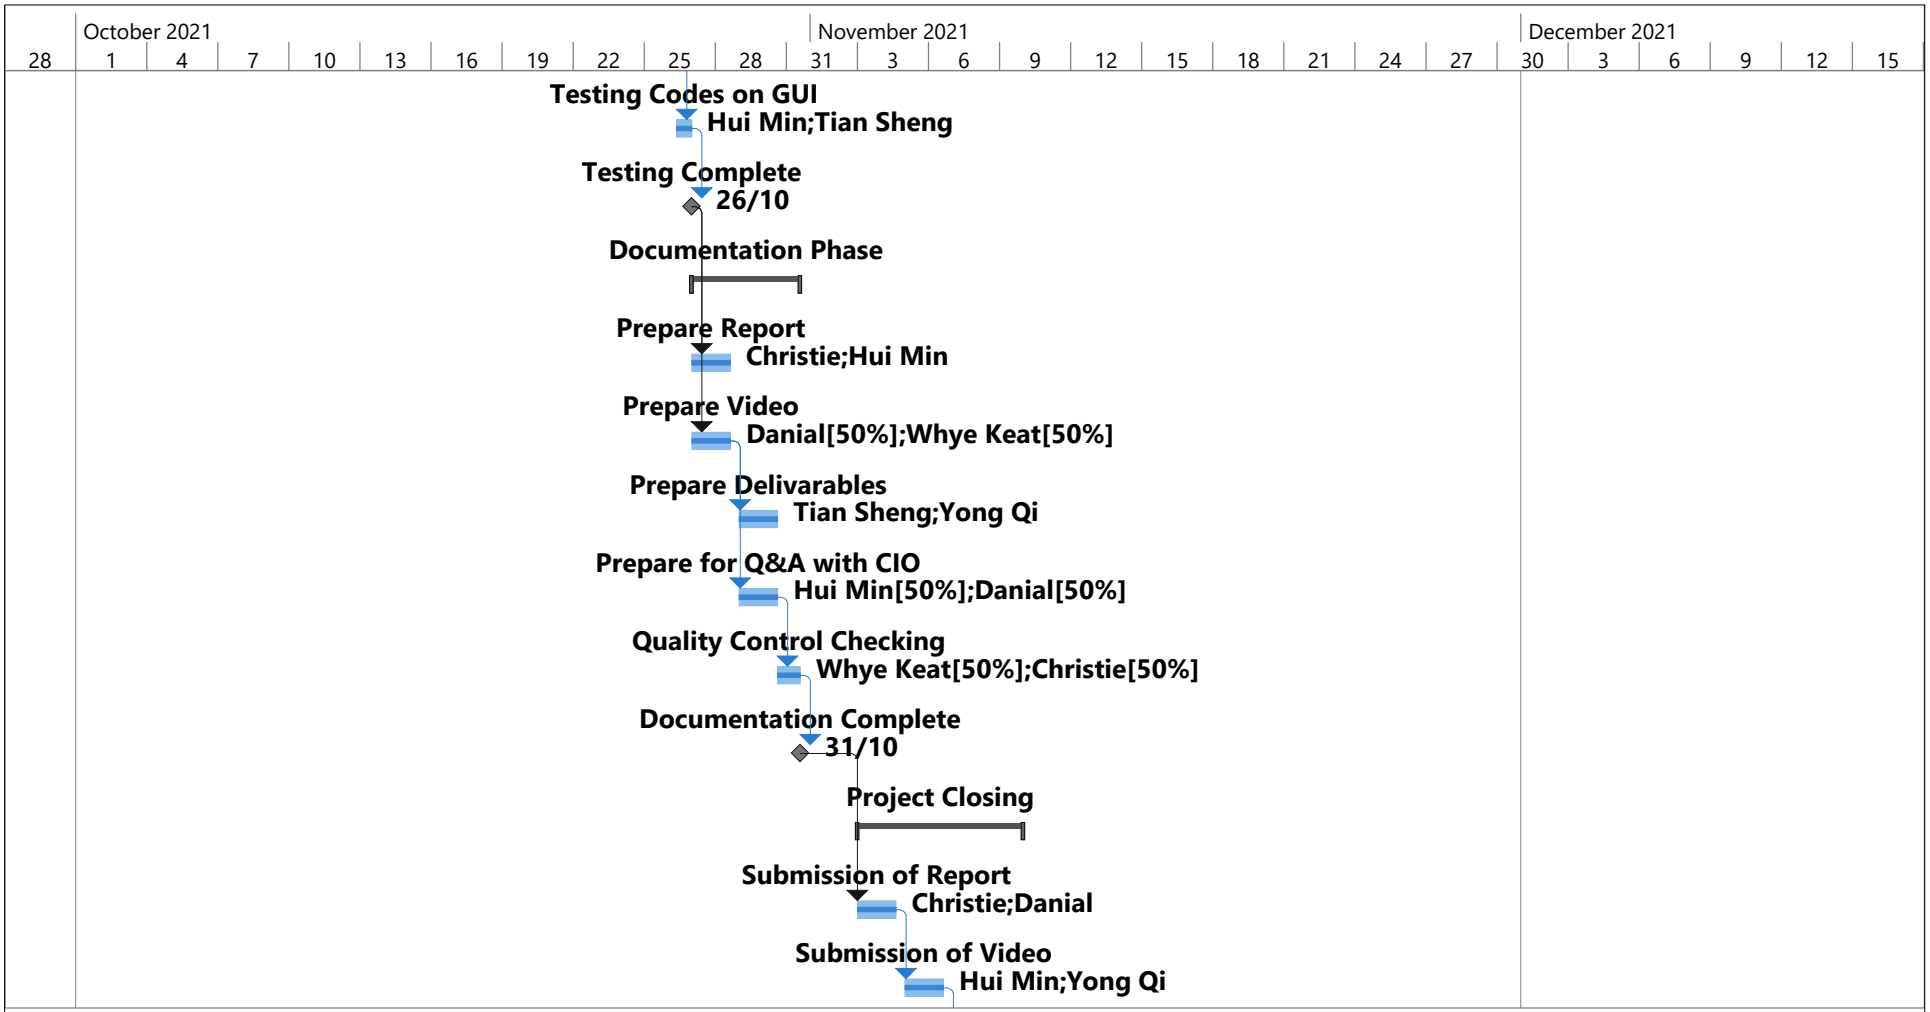

Project: Webook
Date: Fri 12/11/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

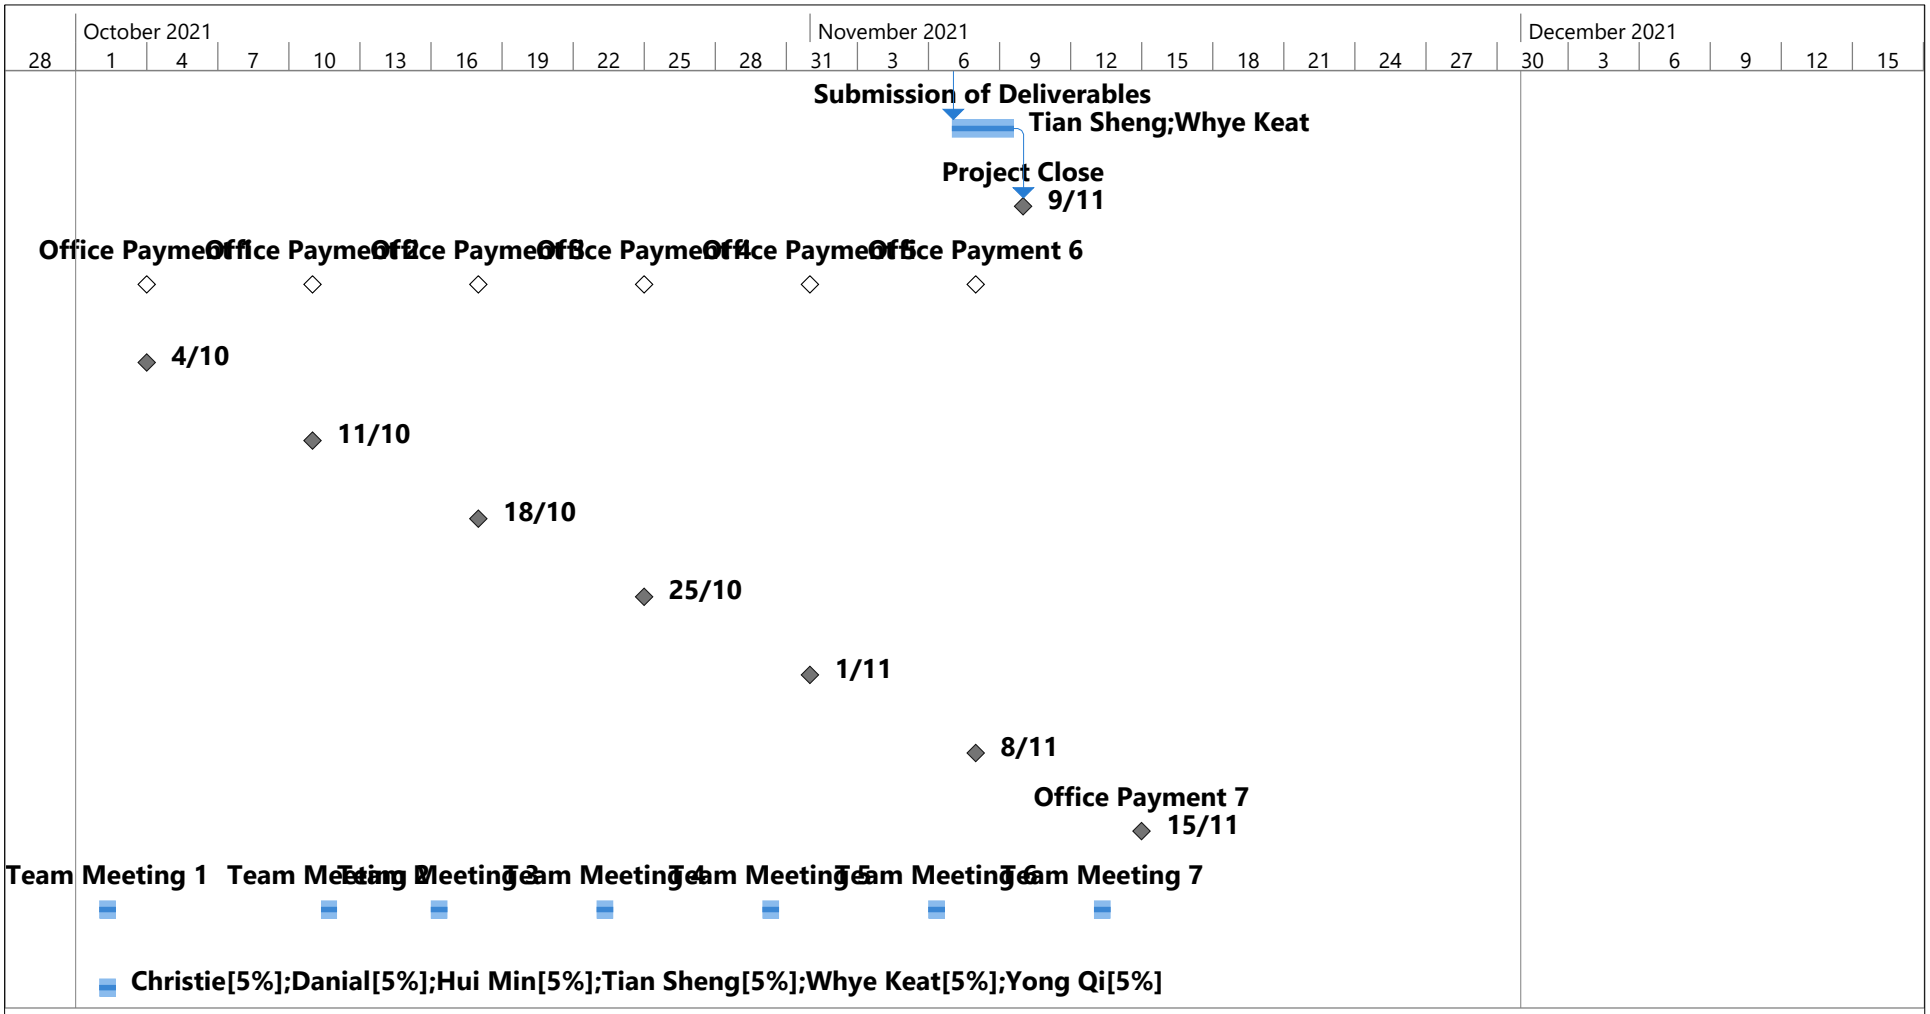

Project: Webook
Date: Fri 12/11/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

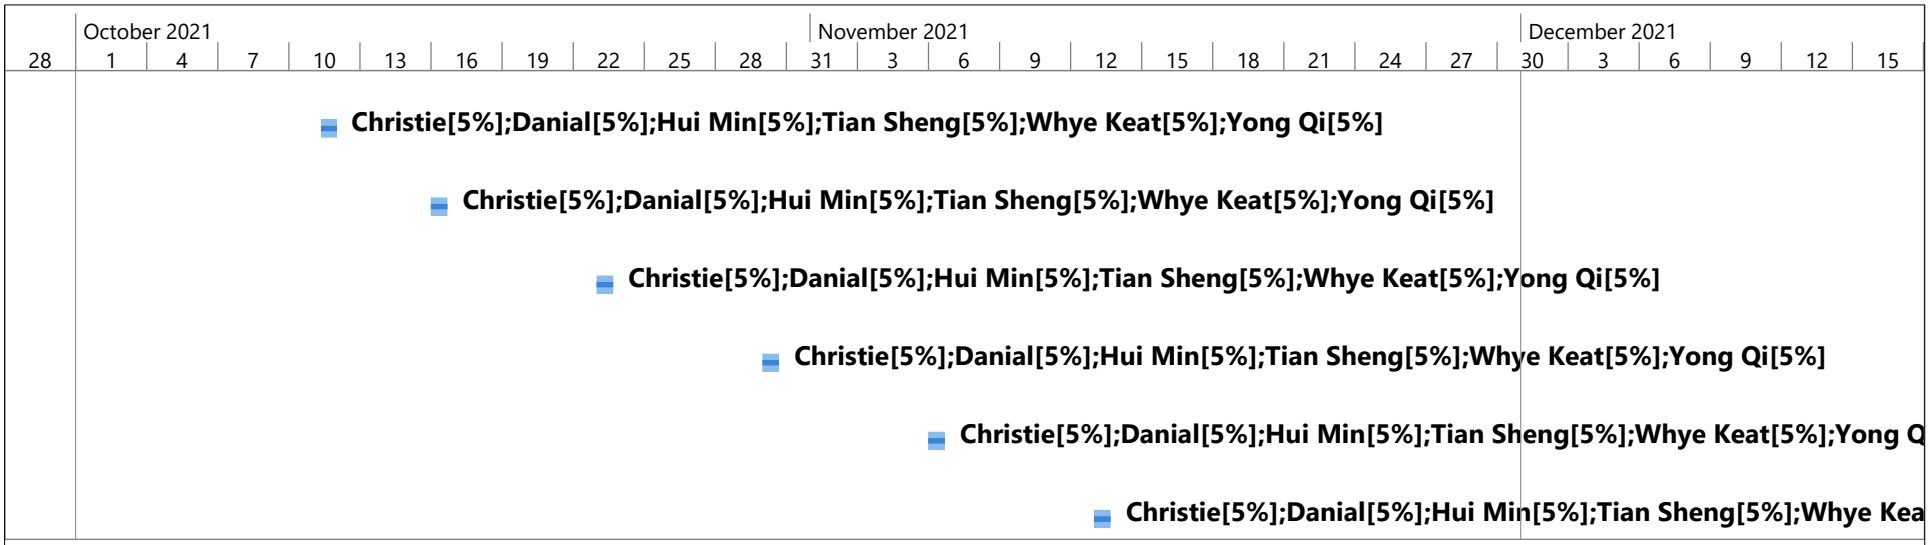

Project: Webook
Date: Fri 12/11/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
